

PROJECT PROPOSAL AND DEVELOPMENT COST VALUATION

AELIA CREATOR COMMERCE PLATFORM

What it takes to design, build, launch and run the Creator Commerce Platform in six months, costed line by line from the team's actual cost, as the investment behind Codevertex's 30% revenue share.

Document	Project Proposal and Development Cost Valuation
Prepared for	Aelia Holdings Limited, attention Erick Wanga
Prepared by	Codevertex Africa Limited, Titus Owuor, Director and Technical Lead
Delivery	Development starts 5 October 2026 · MVP pilot live at month 3 · version 1 live at month 6
Headline figures	Build quotation KES 1,477,218 · total Codevertex contribution KES 2,223,558
Date and validity	26 September 2026 · figures valid for 30 days

BUILD IT · RUN IT · GROW IT · SHARE THE UPSIDE

01 Purpose and Executive Summary

Aelia's board has chosen a revenue-share partnership over a shareholding. Codevertex funds and delivers the build, and in return receives 30% of the platform's net revenue under a legally binding agreement. For that to be fair to both sides, the contribution behind the 30% has to be measured the way a paying client would measure it.

This proposal prices the project as though Aelia were paying for it: the development team for six months from 5 October 2026, the build infrastructure, and the Codevertex platform services the build plugs into. It then sets out, just as plainly, what Aelia pays to run the platform once it is live, and how the net revenue is shared.

The quotation is the team's actual cost, and it covers more than coding. Aelia provides the system requirements; within the same fees, Codevertex's technical lead refines them and prepares the full system design with the Aelia team before the developers start. The same figures give Aelia a solid basis for the return-on-investment section of its business plan.

The arrangement in one paragraph

Codevertex carries the build cost: development and build infrastructure. Aelia carries everything else: marketing, sales, pilot recruitment, and the platform's direct running costs from launch, about KES 8,288 a month for the ERP subscription and domains. Hosting and support after launch are part of Codevertex's share, never billed. What remains after running costs is net platform revenue, shared 70% to Aelia and 30% to Codevertex every month. While the share is being paid there is no repayment deadline; section 15 sets out the only two cases where one applies. Read as a quotation, KES 1,477,218 is the cash Aelia would otherwise have needed upfront.

KES 1,477,218

Build quotation

development team fees, 10% contingency and build infrastructure over 26 weeks

KES 746,340

Platform brought in

Codevertex services Aelia plugs into instead of building, at the same team cost

KES 2,223,558

Total contribution

the investment Codevertex puts in, and the basis for the 30% revenue share

3 and 6

Months to pilot and v1

a real pilot with paying brands at month 3, the full version 1 at month 6

Contingency and build infrastructure · KES 217,218

Development team fees · KES 1,260,000

Platform brought in · KES 746,340

Build quotation, KES 1,477,218

Total Codevertex contribution behind the 30% share, KES 2,223,558

Figure 1. What makes up the investment behind the 30% share. Every figure is broken down line by line in sections 08 to 10.

02 Scope of Work

AREA	MVP PILOT, LIVE AT MONTH 3	VERSION 1, LIVE AT MONTH 6	LATER PHASES, NOT IN THIS QUOTATION
Accounts and access	Single sign-on for brands, creators and Aelia staff; roles and permissions; brand and creator verification	Two-step login for admins, full audit log, access review	Nothing further needed
Brand and Creator Passports	Creator Passport v1 with verified creator details; Brand Passport v1 with organisation details	Passport v2 with track record, platform history and connected social account metrics	Deeper audience analytics
Campaigns	Brief builder with content rights; admin-curated shortlist; workspace and messaging; submission, revisions, approval	Rules-based matching; ratings and reviews; rebooking; improvements from pilot feedback	Full AI matching engine trained on platform data
Money and tax	M-Pesa and card funding; commission ledger; creator payouts with starting fee and balance; bank transfer with proof upload and finance verification; configurable tax engine	Monthly withholding certificates; configurable fee settings	Other currencies and countries, already a per-account setting from day one
AI-generated content	Handled as a managed service by AELIA Creative & Digital	Integrated AI video tools with automatic cost per clip; posting on Aelia's own channels	More AI tools and formats
Insight and administration	Basic dashboards and verification queue	Brand reporting and campaign insights; full admin console for disputes and moderation	Advanced analytics
Channels	Mobile-first web app that installs to a phone's home screen, with public landing and sign-up pages	Same, hardened and load tested	Native Android and iOS store apps
Operations	Development, staging and production environments; automated deployment; monitoring; backups	Security and data-protection review; load test; restore drill; runbooks; handover training; two weeks of close post-launch support	Nothing further needed

What this quotation covers

Aelia Brand House has three arms: AELIA Marketing, AELIA Creative & Digital with its Academy, and the Creator Commerce Platform. This quotation covers the Creator Commerce Platform and its dedicated site. The general Brand House website that introduces all three arms is a separate, smaller build and is quoted separately.

03 How the Platform Plugs Into Codevertex

Aelia gets its own platform, built new around brands and creators working together. Everything underneath it that every serious platform needs, and that Codevertex already runs in production for businesses across Kenya, is plugged in rather than rebuilt. That is where the time and cost saving comes from, and it is also why one partner can build, host, secure and keep improving the platform without Aelia hiring a separate consultant for each job.

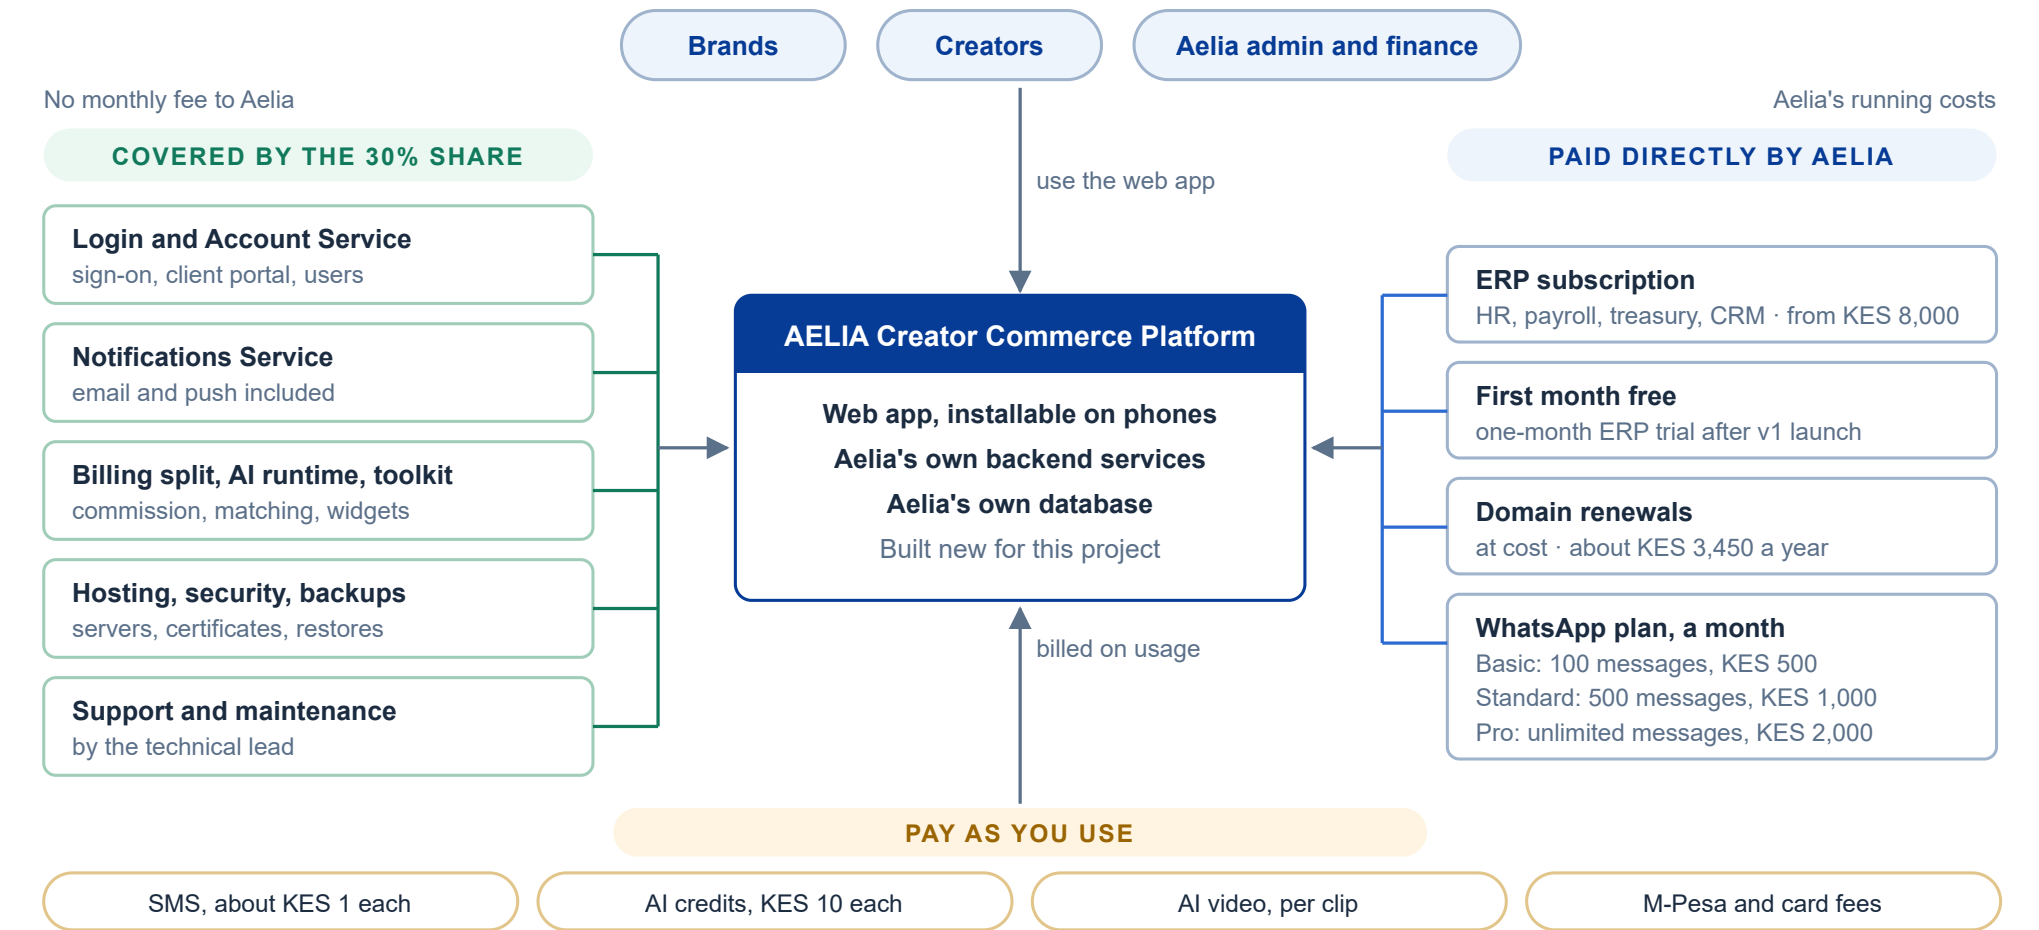


Figure 2. Everything on the left, including hosting and support after launch, is covered by Codevertex's 30% share. Aelia pays the items on the right directly, and pay-as-you-use items only when used.

04 The Team and How We Work Together

Titus Owuor
TECHNICAL LEAD, BACKEND AND INFRASTRUCTURE

Director of Codevertex Africa. Refines Aelia's requirements and prepares the system design. Owns the architecture, payments, commission and tax logic, security, infrastructure and releases. Reports progress to Aelia every week. Oversees critical technical decisions and makes recommendations on them; those decisions are taken jointly with Aelia.

86 planned days all 26 weeks 70.5% loaded

Steve Oginga
BACKEND ENGINEER

Builds the platform's services: onboarding, Passports, campaigns, messaging, payouts, tax, reporting, and the connections into the Codevertex services the platform plugs into.

101 planned days all 26 weeks 82.8% loaded

Meshack Isava
FRONTEND ENGINEER

Builds everything people see and touch: the design system in AELIA's brand, the brand and creator journeys, dashboards, the admin console, and the installable phone experience.

100 planned days all 26 weeks 82% loaded

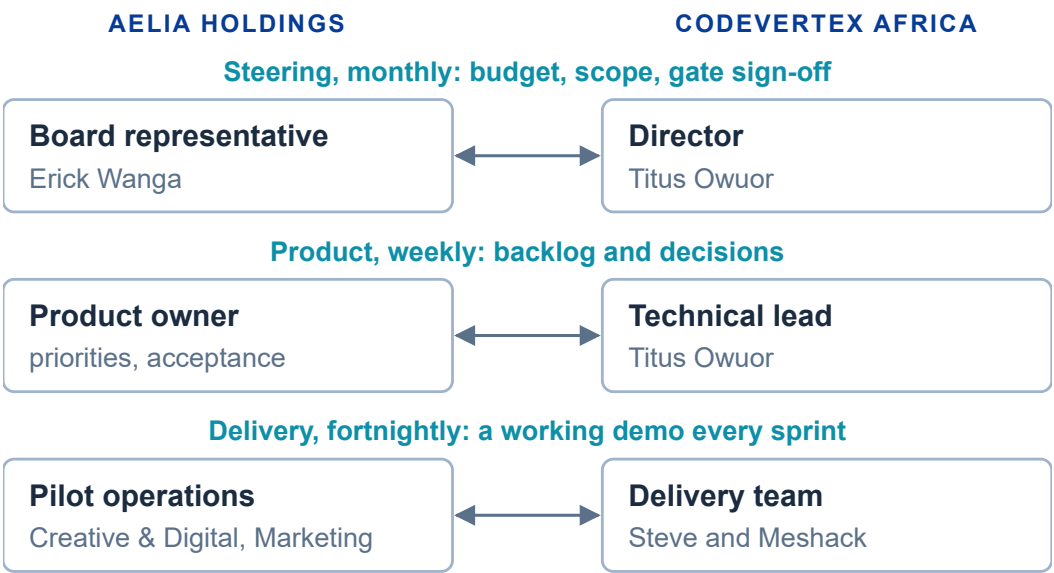


Figure 3. Three levels of contact, each with a fixed rhythm.

RESPONSIBILITY	AELIA	TITUS	STEVE	MESHACK
Product priorities and backlog order	A	C	C	C
Critical technical decisions	A jointly	R, A jointly	C	C
Backend services and integrations	I	A	R	I
Web app and user experience	C	A	C	R
Infrastructure, security, releases	I	A, R	C	C
Payment, commission and tax logic	C	A, R	R	I
Pilot recruitment and onboarding	A, R	C	I	I
User acceptance testing	A, R	R	C	C

R does the work · A is accountable and signs off · C is consulted · I is kept informed

05 Delivery Methodology

Agile delivery in 13 two-week sprints, with a working demo at the end of every sprint and five formal gates where Aelia signs off before the next stage starts.




Figure 4. Every sprint follows the same ten working days.

Definition of Done, for every feature

- Meets the acceptance criteria Aelia agreed at sprint planning
- Code reviewed by a second engineer; automated tests pass
- Payment, commission and tax code has at least 70% test coverage
- Deployed to staging automatically and checked on a phone and a laptop
- No known high or critical security issue left open
- Demonstrated to Aelia and accepted

How Aelia stays informed

- A short written update every Friday: done, next, anything blocked
- A live demo of working software at the end of every sprint
- A shared project board Aelia can open at any time
- A monthly steering meeting on budget, scope and the next gate
- A named contact for urgent questions: Titus Owuor

Change control

New ideas are welcome at any point. Each one is costed within three working days at the same team cost per day used in this proposal, so Aelia always knows the effect on time and cost before saying yes.




Figure 5. Approved changes are added to the contribution, or invoiced if Aelia prefers to pay for them directly.

06 **Delivery Plan and Team Loading**



G1 Environments live, week 2 · G2 MVP pilot live, week 13 · G3 Feature complete, week 22 · G4 User testing signed off, v1 live, week 24 · G5 Handover, week 26

Figure 6. Requirements and design (amber) are finished before the developers start. Build phases then overlap so building and testing run side by side: dark blue phases build the MVP pilot, teal phases build version 1. Costs in KES.

TEAM MEMBER	UP TO THE PILOT, WITH PHASE D	AFTER THE PILOT, WEEKS 14 TO 26	WHOLE PROJECT
Titus Owuor, technical lead	44 days · 72.1% loaded	42 days · 68.9% loaded	86 of 122 available days · 70.5%
Steve Oginga, backend engineer	47 days · 77% loaded	54 days · 88.5% loaded	101 of 122 available days · 82.8%
Meshack Isava, frontend engineer	51 days · 83.6% loaded	49 days · 80.3% loaded	100 of 122 available days · 82%

Available days allow for public holidays, including the December break, and leave. No one is planned above 90% in any window, which leaves room to absorb the unexpected without moving a gate.

07 Phases, Deliverables and Exit Criteria

Each phase ends with something Aelia can see working, and a clear test that has to pass before the next gate. Days are shown for Titus, Steve and Meshack in that order.

PHASE	DELIVERABLES	EXIT CRITERIA AND GATE	DAYS T / S / M	KES
D · Requirements and system design BEFORE 5 OCTOBER	Aelia's requirements refined into an agreed specification with acceptance criteria; system design covering architecture, data, service interfaces and integrations; screen flows; a ready build backlog	Requirements and design signed off by Aelia, so developers start on 5 October with nothing left to guess	10 / 0 / 0	43,903
P0 · Setup and foundations WEEKS 1 TO 2	Development, staging and production environments on accounts Aelia owns; automated deployment and monitoring; design system in AELIA's brand; single sign-on working	G1: environments live. Every change deploys to staging automatically. A test brand and a test creator can sign in	9 / 4 / 8	92,196
P1 · Brand and Creator core WEEKS 2 TO 6	Brand onboarding and verification; creator onboarding; Creator Passport v1; Brand Passport v1; admin verification queue and user management	A brand and a creator register, are verified by an Aelia admin, and see their Passports. Demo accepted	3 / 15 / 15	144,878
P2 · Campaigns and marketplace WEEKS 5 TO 9	Brief builder with content rights; discovery and admin-curated shortlist; campaign workspace and messaging; submission, revision and approval; notifications at every step	A full campaign runs in staging from brief to approved content, with notifications firing at each step	1 / 12 / 15	122,927

Pilot build and version 1

PHASE	DELIVERABLES	EXIT CRITERIA AND GATE	DAYS T / S / M	KES
P3 · Payments and MVP pilot launch WEEKS 8 TO 13	M-Pesa and card funding; commission ledger; creator payouts with starting fee and balance; bank transfer with proof upload and finance verification; configurable tax engine; dashboards; production go-live	G2, pilot live: a real campaign is funded, delivered, approved and paid out in production, and the ledger reconciles to the shilling	21 / 16 / 13	219,511
P4 · Intelligence, reputation and AI content WEEKS 14 TO 22	Rules-based matching; Passport v2 with social account connections; brand reporting; withholding certificates; ratings and rebooking; fee settings; AI-generated content with automatic cost per clip; pilot improvements	G3, feature complete: every brief gets a ranked shortlist, every AI clip is costed automatically, pilot feedback is triaged every sprint	22 / 34 / 33	390,732
P5 · Hardening, user testing and v1 launch WEEKS 21 TO 26	Admin console for disputes, moderation and audit; security and data-protection review; load test; backup and restore drill; user acceptance testing; documentation and training; launch and two weeks of close post-launch support	G4: user testing signed off and v1 live. G5: handover complete, zero open high or critical security findings, restore proven within 4 hours	20 / 20 / 16	245,853

08 **How the Price Is Built**

The quotation is the team's actual cost for the six months from 5 October 2026, with nothing added for overhead. Fixed monthly fees mean the cost does not grow with hours worked. It works out at about KES 4,390 per planned team day, the figure used for every work package, the platform brought in and any approved change.

COST LINE	MONTHLY	PERIOD	KES
Development team: technical lead, backend engineer, frontend engineer	KES 210,000 a month	6 months	1,260,000
Contingency, 10% of team fees, used only with Aelia's written approval			126,000
Build infrastructure and tools, at published prices			91,218
Build quotation			1,477,218
VAT: not charged			0

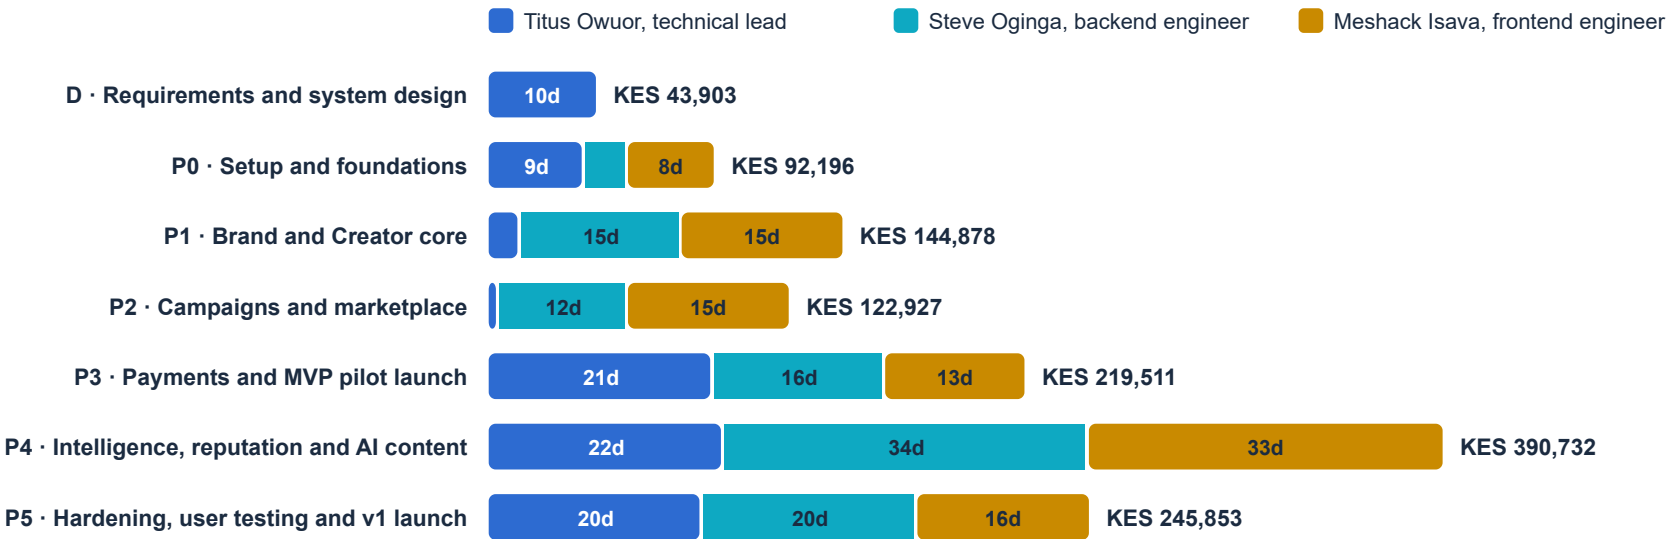


Figure 7. Days per person in each phase, with the phase's cost, across 39 work packages.

Design and build, one price

The same fees cover refining Aelia's requirements, the full system design, and then building, testing and launching the platform.

Where the money goes

About half the team fees, KES 623,415, are spent up to the pilot, phases D to P3, so Aelia has a working, earning platform at month 3.

Why contingency is included

Every build meets surprises, such as a payment provider changing an approval step. Ten percent is the lower end of normal practice for a fixed plan.

09 Work Breakdown: Pilot Build, Days per Person

WORK PACKAGE	TITUS	STEVE	MESHACK	DAYS	KES
D • Requirements and system design					43,903
Requirements refinement with the Aelia team: gaps, priorities, acceptance criteria	4	–	–	4	17,561
System design: architecture, data design, service interfaces, integrations	4	–	–	4	17,561
Screen flows and a ready build backlog for the developers, reviewed with Aelia	2	–	–	2	8,781
P0 • Setup and foundations					92,196
Environments, automated deployment, AELIA-owned accounts, secrets, monitoring	7	1	–	8	35,122
AELIA design system, app shell, landing and sign-up pages, installable app base	–	–	6	6	26,342
Single sign-on with the shared login screen, roles and permissions	2	3	2	7	30,732
P1 • Brand and Creator core					144,878
Brand onboarding, organisation profile, verification workflow	1	5	4	10	43,902
Creator onboarding and Creator Passport v1 with verified details	1	5	5	11	48,293
Brand Passport v1 (organisation and verification)	–	2	2	4	17,561
Admin foundations: verification queue, user management, configuration	1	3	4	8	35,122
P2 • Campaigns and marketplace					122,927
Campaign brief builder with content rights	1	3	4	8	35,122
Creator discovery, search and admin-curated shortlist	–	2	3	5	21,951
Campaign workspace and messaging v1	–	3	4	7	30,732
Content submission, revisions, approval	–	3	4	7	30,732
Notifications at each campaign step	–	1	–	1	4,390
P3 • Payments and MVP pilot launch					219,511
M-Pesa and card payments, campaign funding	6	3	3	12	52,683
Per-transaction commission ledger and reconciliation	6	3	–	9	39,512
Creator payouts, starting-fee and balance schedules	1	3	2	6	26,341
Manual bank transfer with proof upload and finance verification	–	3	3	6	26,341
Configurable tax engine (work categories and rates)	4	1	1	6	26,341
Transaction statuses and basic dashboards	–	1	2	3	13,171
Pilot deployment, production hardening, go-live support	4	2	2	8	35,122

09 Work Breakdown: Version 1, Days per Person

WORK PACKAGE	TITUS	STEVE	MESHACK	DAYS	KES
P4 · Intelligence, reputation and AI content					390,732
Rules-based matching v1, then refinement from pilot data	7	6	2	15	65,854
Creator and Brand Passport v2: track record and platform history	–	3	4	7	30,732
Reporting, performance data, campaign insights for brands	–	4	7	11	48,293
Monthly withholding certificates	1	1	1	3	13,171
Messaging, discovery and brief enhancements from pilot feedback	–	3	3	6	26,341
Two-sided ratings and reviews	–	3	4	7	30,732
Rebooking flow	–	3	2	5	21,951
Revenue tracking and configurable fee settings	–	3	2	5	21,951
AI-generated content lane: AI video tools, automatic cost per clip	7	3	3	13	57,073
Social account connections for Creator Passport metrics	4	2	2	8	35,122
Pilot support and iteration	3	3	3	9	39,512
P5 · Hardening, user testing and v1 launch					245,853
Full admin console: disputes, moderation, audit log	–	5	6	11	48,293
Security and data-protection review, fixes, access review	6	3	–	9	39,512
Load testing, backup and restore drills	4	2	–	6	26,341
User acceptance testing with pilot brands and creators, fixes	3	4	5	12	52,683
Documentation: technical guides, runbooks, admin guide, handover training	4	3	2	9	39,512
Launch and two weeks of close post-launch support	3	3	3	9	39,512
Total development team fees	86	101	100	287	1,260,000

10 Build Infrastructure and the Platform Brought In

BUILD INFRASTRUCTURE	BASIS, AT PUBLISHED PRICES	KES
Staging and testing environment	A 4 GB cloud server at USD 48 a month for 6 months, DigitalOcean list price	37,440
Automated build and deployment	GitHub Team at USD 4 per user a month, 3 users, 6 months, for protected branches, review rules and extra build minutes	9,360
AI video tool testing	Creatify Pro at USD 99 a month for months 4 to 6, while the AI content lane is built	38,610
SMS and WhatsApp testing	About 1,500 test SMS at about KES 1 each, plus a Basic WhatsApp plan at KES 500 a month for 3 months	3,000
Production capacity during build and pilot	About 8% of Codevertex's managed production cluster for 6 months	2,808
Total		91,218

Codevertex platform brought in, at replacement value

The value of each service is based on the effort the same team would need to build it to the standard this platform needs, priced at the same cost per team day as the build. Aelia pays no licence fee for any of it. It is counted as part of Codevertex's contribution because it is real, running software that Aelia would otherwise have to build and pay for.

SERVICE	WHAT AELIA GETS WITHOUT BUILDING IT	DAYS SAVED	KES
Login and Account Service	Single sign-on, two-step login for admins, client portal, people who belong to several businesses, roles	37	162,439
Payments Service	M-Pesa and card collection, payment confirmations, payouts to third parties, reconciliation, KRA eTIMS invoicing, manual payment confirmation	46	201,951
Billing Service	Plans, feature switches, and the engine that splits each payment between parties	22	96,585
Notifications Service	Email, SMS, WhatsApp and push from one call, message templates, prepaid SMS credits and WhatsApp plans	18	79,024
Shared toolkit and UI library	Ready-made login and payment screens, service connections, event messaging, caching	18	79,024
Managed platform infrastructure	Managed servers, secure web addresses with automatic certificate renewal, deployment pipelines, monitoring, logs, backups	14	61,463
AI assistant runtime	The AI assistant engine reused for creator matching and the brief builder	15	65,854
Total platform brought in		170	746,340

11 **Total Contribution and What the 30% Pays For**




Figure 8. Labour only. Building from scratch costs about KES 746,340 more, and roughly 20 more weeks of backend work would push the pilot from month 3 to around month 8.

CODEVERTEX CONTRIBUTION	KES
Development team fees	1,260,000
Contingency	126,000
Build infrastructure and tools	91,218
Build quotation	1,477,218
Platform brought in, replacement value	746,340
Total contribution behind the 30% share	2,223,558

What the 30% share pays for

Capital and risk

Codevertex funds the whole build, KES 1,477,218 of team fees, contingency and infrastructure, paying the team every month from week 1 with no guaranteed return. If the platform earns little, Codevertex earns little.

A running platform, not a blank page

Software already live in production for businesses across Kenya, plus every future improvement to those shared services, passed to Aelia at no extra cost.

Support for the life of the partnership

After launch, Codevertex's technical lead looks after the platform, its security and the AI content lane at no extra charge. The 30% share is Codevertex's only payment for this.

12 Running the Platform After Launch

WHO PAYS	ITEM	KES A MONTH
IN THE 30% SHARE	Support and maintenance by Codevertex's technical lead: monitoring, security patches, fixes, backups, running the AI content lane	KES 0
IN THE 30% SHARE	Login and Account Service, Notifications Service, billing split, AI assistant runtime, shared toolkit	KES 0
IN THE 30% SHARE	Hosting the AELIA platform: production servers, security certificates and renewals, backups and server oversight, handled by Codevertex	KES 0
AELIA, FIRST MONTH FREE	ERP starting suite for Aelia's own team, up to 25 employees and 10 system users, covering HR, payroll, CRM, and treasury with payments, payouts, invoicing and KRA eTIMS. One-month free trial after version 1 launch, instead of the standard 14 days	from 8,000
AELIA, AT COST	Domain renewals for the platform's own addresses: a .com at about USD 15 and a .co.ke at about KES 1,500, KES 3,450 a year	288
AELIA, IF USED	WhatsApp plan: Basic KES 500 for 100 messages, Standard KES 1,000 for 500 messages, or Pro KES 2,000 for unlimited messages	500 to 2,000
PAY AS YOU USE	SMS about KES 1 each · AI credits KES 10 each · M-Pesa and card fees at the providers' published rates	usage
PAY AS YOU USE	AI video tools: KES 1,150 to 1,770 all-in per clip, recovered in a brand price that starts from KES 5,000	per clip

KES 8,288

Aelia's fixed monthly running cost

ERP subscription and domains; hosting is covered by the 30% share. It is KES 288 in the first month after launch, during the ERP free trial.

Support after launch, inside the 30%

- Round-the-clock uptime monitoring and alerts
- Security patches, updates and certificate renewals
- Daily backups and quarterly restore tests
- Bug fixes, with critical issues answered within 2 hours
- Running the AI-generated content pipeline
- Small improvements as the platform grows
- A monthly health report to Aelia

As Aelia's team grows

KES 8,000 covers up to 25 employees, about KES 320 each, with treasury and CRM included. HR tools alone cost from about KES 135 a user on Zoho People to about KES 650 an employee on Workpay. Beyond 25 employees, HR and payroll move to a per-employee enterprise rate agreed by both sides, guided by the Kenyan market range of KES 100 to 400 per employee a month for cloud HR and payroll software. At an illustrative KES 250, a team of 40 would add KES 3,750 a month.

Larger new features are costed at the same team cost per day.

13 How the Revenue Share Works

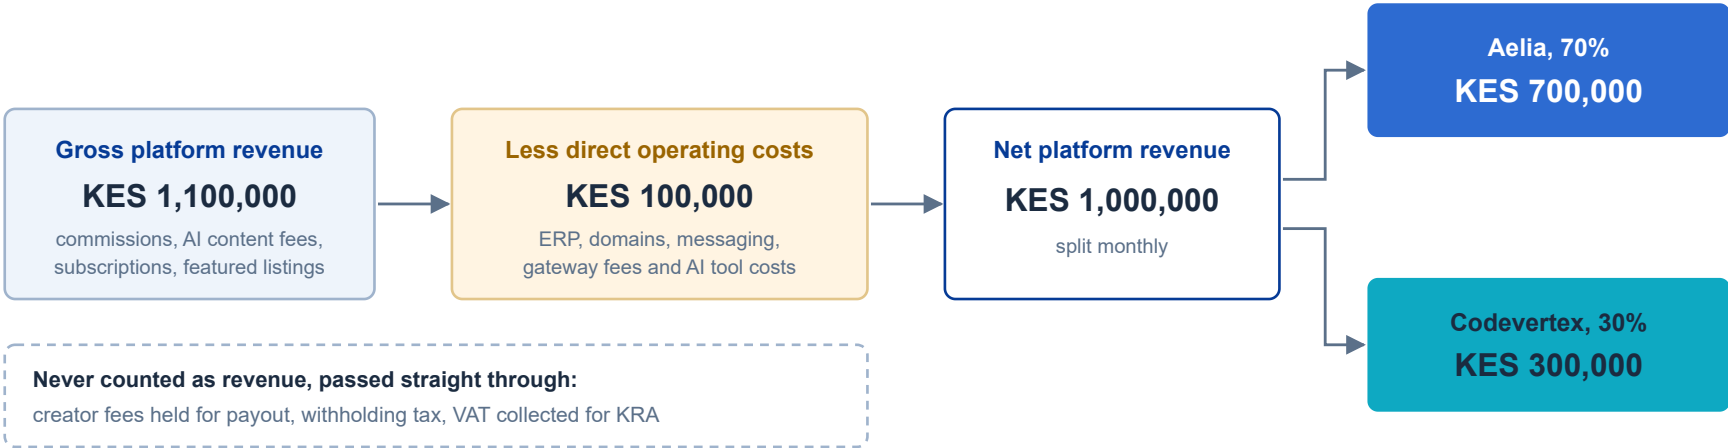


Figure 9. One illustrative month. The same three steps run every month, from a statement generated directly from the platform's own ledger.

Gross platform revenue

Everything the platform itself earns: commission on campaigns, AI-generated content fees, subscriptions, featured listings, and any new revenue line added later. Money that belongs to creators, and taxes collected for KRA, pass straight through and are never counted.

Direct operating costs

Only the costs of running this platform: the ERP subscription, domains, messaging, gateway fees and AI tool costs. Hosting, support and maintenance are not deducted; they are part of Codevertex's 30%. Aelia's wider overheads such as rent, salaries and marketing are not deducted either.

The monthly split

Net platform revenue is split 70% to Aelia and 30% to Codevertex, paid within 15 days of month end. Both sides see the same numbers, because the statement comes from the platform's own records, not from a spreadsheet.

WHAT MADE UP THE KES 100,000 IN FIGURE 9	KES
ERP subscription with HR, payroll, treasury and CRM	8,000
Domain renewals, monthly share	288
WhatsApp and SMS, AI credits, gateway fees, AI video tools	91,712
Direct operating costs	100,000

When each charge starts

- **Weeks 1 to 26:** no development or infrastructure charges
- **Pilot, months 3 to 6:** only pay-as-you-use items, billed at cost
- **From version 1 launch:** domain renewals, at cost
- **ERP subscription:** free for the first month after launch, then KES 8,000 a month
- **Hosting and support after launch:** never billed, covered by the 30% share
- **First revenue-share statement:** the first full month after version 1 launch

14 **Payback and Return on Investment**

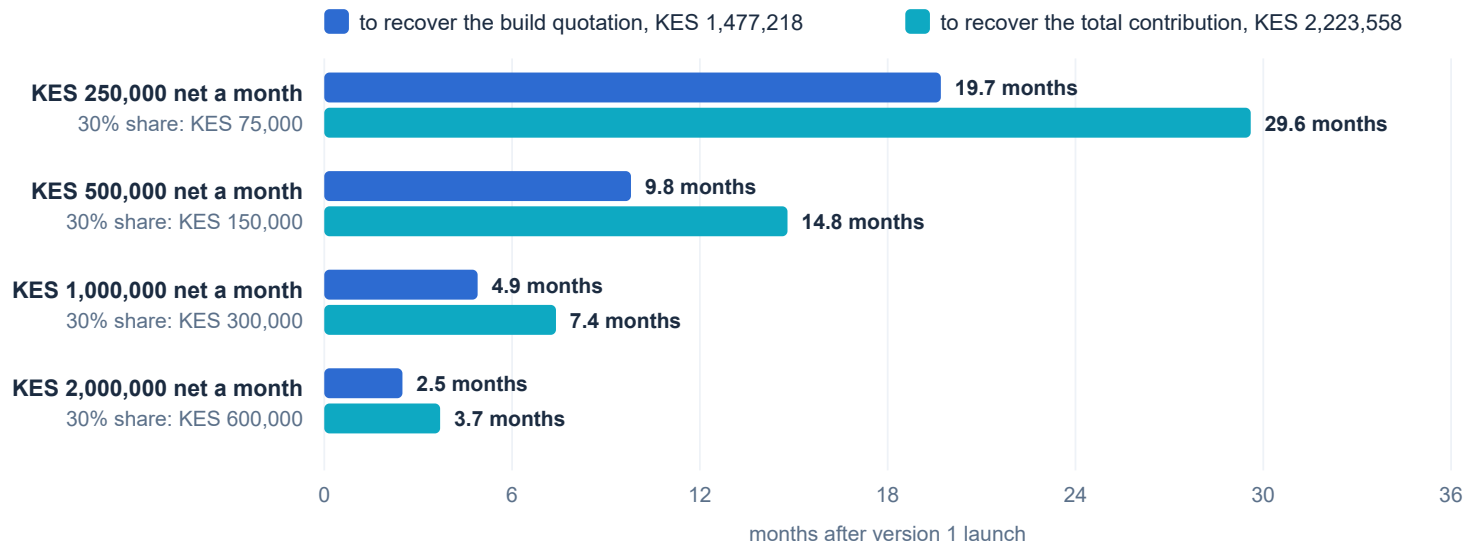


Figure 10. How long Codevertex's 30% share takes to recover the investment. The more the platform earns, the sooner Codevertex is repaid.

Aelia's position

Aelia puts in no development capital, so its 70% is earned on running costs alone. Instead of finding KES 1,477,218 upfront, Aelia has a live platform at month 3 and pays about KES 8,288 a month to run it from version 1. At KES 1 million net a month, Aelia keeps KES 700,000 a month, KES 8.4 million a year.

Codevertex's risk

A new marketplace usually earns little in its first year. At KES 250,000 net a month, the 30% share takes about 30 months to repay the full contribution. The 30% prices in that risk, and section 15 sets out how the build cost is handled if revenue stays slow.

A planning marker for the business plan

Using the 8% commission in Aelia's own concept paper, the platform covers its fixed running cost at about KES 103,600 of campaign value a month, roughly 5 campaigns of KES 20,000. It reaches KES 1 million net at about KES 12.6 million of campaign value a month, before other revenue lines.

15 If Revenue Is Slow: Protecting the Build Investment

As long as the 30% share is being paid, there is no repayment timeline at all: the share itself recovers the build cost, however long that takes. A timeline applies in only two cases: if the platform earns no net revenue for a sustained period, or if Aelia chooses to part ways before the build cost is recovered.

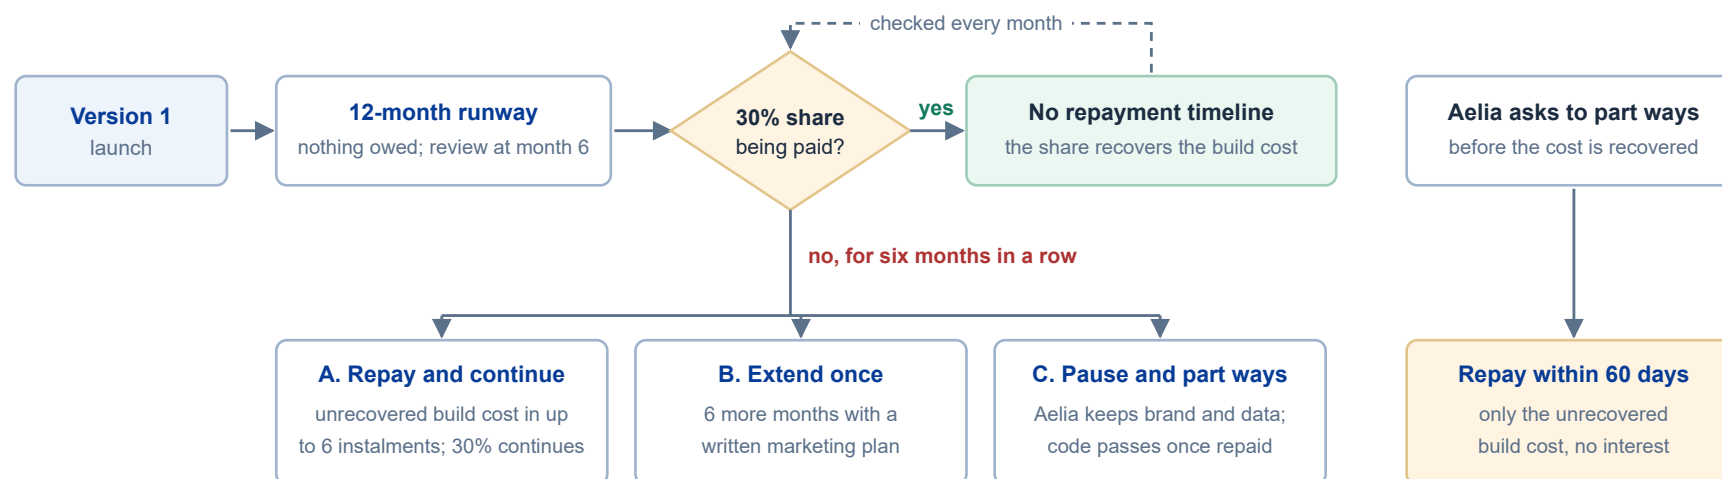


Figure 11. The 30% share replaces any repayment deadline. Repayment only comes into play in the two cases on the right and below. Details on the next page.

What is being protected

The build quotation, KES 1,477,218: real cash Codevertex pays out during the build. The platform brought in is not counted here, so any repayment never exceeds what was actually spent.

Worked example

After the runway, the platform goes six months in a row with no net revenue. Codevertex has received KES 300,000 in share so far, so the unrecovered build cost is KES 1,177,218. Under option A, Aelia repays it in six instalments of KES 196,203, and the 30% share continues.

Aelia's go-to-market commitments

Because recovery depends on marketing, Aelia commits to a named marketing lead, a written launch plan and budget before version 1 launch, the pilot recruitment targets in section 16, and a short monthly marketing report.

15 If Revenue Is Slow: Proposed Terms

POINT	CODEVERTEX'S PROPOSED POSITION
The share replaces any deadline	While the 30% share is being paid, Aelia has no repayment obligation and no deadline of any kind. The build cost is recovered through the share alone, however long that takes.
Revenue runway	The first twelve months after version 1 launch. Nothing is owed on the build cost during this time, whatever the platform earns.
Joint review, month 6	If net platform revenue is not yet covering the platform's running costs, both parties will agree a written recovery plan within 30 days, for example a marketing push, pricing changes or a narrower focus. The review creates no payment obligation.
No-revenue trigger	This applies only after the runway. If the platform produces no net revenue, so that no 30% share is payable, for six consecutive months, Aelia will choose option A, B or C within 30 days. Any month in which a share is payable resets the count.
Option A: repay and continue	Aelia repays the unrecovered build cost, meaning the build quotation less all share already paid, in up to six monthly instalments with no interest. The 30% share then continues as agreed, with Codevertex remaining the technology partner.
Option B: extend once	The trigger period is extended once by six months, backed by a written marketing plan and budget from Aelia. If no share has become payable by the end of the extension, Aelia will choose option A or C.
Option C: pause and part ways	The platform is paused and running costs stop. Aelia keeps its brand, customer relationships and data. Aelia may pay the unrecovered build cost at any time, and the platform code then passes to Aelia.
Parting ways early	If Aelia ends the partnership, or moves the platform to another developer, before the build cost is recovered, Aelia will repay the unrecovered build cost within 60 days.
If Codevertex delivers late	If the pilot or version 1 is delayed for reasons within Codevertex's control, the runway starts later by the same period. If version 1 is not live by the end of month 9 after development starts, Aelia may exit without owing any build cost.

16
Key Performance Indicators

Delivery: how Codevertex is measured

INDICATOR	TARGET
Gates met on schedule	Pilot live in week 13, v1 live in week 24
Sprint reliability	85% or more of committed work done each sprint
Test coverage on payment, commission and tax code	70% or more
Platform uptime from pilot launch	99.5% or more a month
Page and API speed	95% of requests answered in under 0.5 seconds
Security	Zero open high or critical findings at launch
Recovery	Service restored within 4 hours, at most 24 hours of data at risk
Ledger accuracy	Payouts and commission reconcile to the shilling every month
Critical support response	Within 2 hours, any day

Pilot: how the idea is proven, months 3 to 6

INDICATOR	TARGET
Brands onboarded and verified	8 to 10
Creators onboarded with a verified Passport	15 to 20
Campaigns run end to end	5 or more
Paid transactions through the platform	3 or more
Content delivered on time	90% or more
Brands intending to book again	2 or more

Growth, after version 1

INDICATOR	WHY IT MATTERS	REPORTED
Monthly campaign value	The base every commission is earned on	Live dashboard
Active brands and creators	Health of both sides of the marketplace	Live dashboard
Repeat booking rate	Proof that brands get value and come back	Monthly
AI-generated content orders	Growth of the fastest-margin lane	Monthly
Net platform revenue	What both partners actually share	Monthly statement

Every indicator comes straight from the platform's own records, so Aelia and Codevertex always read the same numbers.

17 Points to Settle in the Revenue-Share Agreement

POINT	CODEVERTEX'S PROPOSED POSITION
Revenue definition	Net platform revenue is gross platform revenue less the agreed direct operating costs, as set out in section 13. Creator funds and taxes are never counted as revenue.
Deductible costs	Only costs on a fixed list attached to the agreement may be deducted: the ERP subscription, domains, messaging, gateway fees and AI tool costs. Any new cost line needs both parties' written approval.
Hosting and support	Platform hosting, and support by Codevertex's technical lead, are part of the 30% share. They are never invoiced and never deducted as an operating cost.
ERP as Aelia grows	KES 8,000 a month covers the starting suite for up to 25 employees. Above that, HR and payroll are charged per employee at an enterprise rate agreed by both sides, guided by the Kenyan market range of KES 100 to 400 per employee a month.
Reporting and audit	A monthly statement is generated from the platform ledger. Codevertex has read access to the platform's finance dashboards, and either party may audit the figures once a year.
Payment	The share is paid monthly by bank transfer, within 15 days of month end. No share is payable for a month with no net revenue, and a loss in one month is not carried into the next.
Build cost recovery	Governed by section 15. No repayment deadline applies while the 30% share is being paid.
Term	Runs for as long as the platform operates, with a minimum of five years from version 1 launch.
Buyout	From year three, Aelia may buy out the share for three times the previous twelve months' share, never below any unrecovered build cost. After a buyout, support continues under a separate paid support agreement.
New features	New features are priced at this proposal's cost per team day and are either invoiced or, by agreement, added to the contribution.
Continuity	The source code is kept in a repository both parties can access from day one, with full runbooks. If the partnership ends, Codevertex provides 90 days of transition support.

17 Legal Safeguards in the Agreement

Each party should have the final agreement reviewed by its own advocates before signing.

POINT	PROPOSED POSITION
Ownership of the code	Copyright in the platform code stays with Codevertex until the build cost is recovered, through the share or by repayment, and then passes to Aelia by written assignment. The agreement expressly excludes the transfer that section 31 of the Copyright Act would otherwise make to the commissioning party. Until then Aelia uses the code under an exclusive licence. Aelia owns its brand, customers and data from day one; Codevertex keeps the shared services it brings in.
Repayment limit	Any repayment is limited to the unrecovered build cost, with no interest or fees on top.
Revenue kept on the platform	Work with brands or creators first met through the platform counts as platform revenue even if it is completed elsewhere, including through AELIA Marketing or AELIA Creative & Digital. Services between Aelia's own businesses are priced at normal market rates.
Sale or change of control	If the platform or Aelia is sold, the agreement binds the buyer, unless Aelia completes the buyout before the sale.
Taxes	Amounts are stated before any tax that becomes chargeable by law, which is added when it applies. Where the law requires Aelia to withhold tax on payments to Codevertex, Aelia deducts it and issues the withholding certificate within the period the law requires.
Liability	Each party's total liability under the agreement is capped at the revenue share paid in the twelve months before the claim, and neither party is liable for indirect losses such as lost profits. The cap does not apply to fraud, wilful misconduct or payment obligations.
Regulation and licences	Aelia holds the licences its business needs, sets its customer terms and files its own tax returns, including creator withholding. Money moves only through licensed payment providers, and Codevertex never holds client funds.
Late payment	If the share or a repayment remains unpaid 30 days after Codevertex gives written notice, Codevertex may pause new feature work. If it remains unpaid 90 days after the notice, Aelia is treated as having chosen to part ways early.
Data protection	Aelia is the data controller and Codevertex the data processor, under a written data-processing agreement. Each registers with the Office of the Data Protection Commissioner where the law requires it.
Disputes	The directors meet within 14 days of a dispute being raised. An unresolved dispute goes to mediation, and then to arbitration in Nairobi under the rules of the Nairobi Centre for International Arbitration. The agreement is governed by the laws of Kenya.
If Codevertex walks away	If Codevertex ends the partnership without cause, it gives up any unrecovered build cost, and the continuity terms apply.

18 **Assumptions, Exclusions and Commercial Terms**

Assumptions and what Aelia provides

- Complete system requirements from Aelia, refined and signed off together with the system design before 5 October 2026
- A named Aelia product owner, available for weekly decisions and fortnightly demos
- Brand assets, copy and content for the platform's public pages
- Marketing, sales and pilot recruitment led and paid for by Aelia
- Business accounts in Aelia's name: M-Pesa paybill, Paystack, KRA PIN and eTIMS
- Legal review of the terms of service and privacy notice, and registration with the Office of the Data Protection Commissioner
- Scope as set out in section 02; changes follow the change-control process
- The team is retained on fixed monthly fees; if Aelia-side delays extend the build past week 26, each extra month adds KES 210,000

Not included

- Native Android and iOS store apps, a later phase
- The general Aelia Brand House website, quoted separately
- An independent third-party penetration test, if Aelia wants one
- Legal and regulatory fees; paid advertising; content production

Delivery risks and how they are handled

RISK	EFFECT	HOW IT IS HANDLED	OWNER
Payment and tax account approvals take longer than planned	Pilot payments delayed	Applications for M-Pesa, Paystack and KRA eTIMS start in week 1; payments are built and tested in sandbox mode meanwhile	Aelia, with Codevertex
Scope grows during the build	Gates slip, cost rises	Change control with a costed estimate for every request; nothing is added without Aelia's approval	Both
Too few pilot brands or creators	Pilot results are weak	Recruitment starts in month 2 through AELIA Marketing's existing clients and the Academy's creators	Aelia
AI video tool prices change	AI content margin shrinks	Cost per clip is tracked automatically and the brand price is a setting Aelia can change at any time	Codevertex
A team member is unavailable	Work slows	Shared code reviews, written runbooks, and backup from the wider Codevertex engineering team	Codevertex

If the build were invoiced instead

For reference only, the same build as a paid engagement would be invoiced against the gates:

MILESTONE	SHARE	KES
On signing, before work starts	30%	443,165
G2, MVP pilot live, week 13	30%	443,165
G4, user testing signed off and v1 live, week 24	30%	443,165
G5, handover complete, week 26	10%	147,723
Total	100%	1,477,218

All figures in Kenyan shillings. USD figures converted at KES 130. Valid for 30 days from 26 September 2026.

For Aelia Holdings Limited

 Name, signature and date

For Codevertex Africa Limited

 Titus Owuor, Director
